

Presentation Projectplanning, Scope and design

versie 17-1

Projectplanning :


- Aanbesteding -> Thomas van Egmond
- Opdracht
- Vergroten rijwielstalling West + Oost (Hegeman Infra bv)
- Verwijderen perrongebouwen, vernieuwen liften, uitbreiden commerciële ruimten opknappen Stationshal (Hegeman Infra bv)
- Optoppen + transformatie Kantoren naar Woningen Bouwdeel A+B, vernieuwen Winkelpuien (Kroonenberg Groep)
- Opknappen Spoorbaanpad (Gemeente)
- Aanpassen diverse gebouwaansluitingen
- Herinrichten Openbare Ruimte incl. Ondergrondse Infra

Masterplanning :

- Tender (See Thomas van Egmond) – April-August 2022
- Gunning / commission - September 2022
- Fase van controleren DO-ontwerp door Aannemer – max 6 weeks
 - (final design review by construction company)
- Engineering (approx. 5 months)
- Work preparation (approx. 3 months)
- Start foundations (approx. July/August 2023)
- Installation of Steel columns – Q4 in TVP (temporarily decommissioned tracks)
- Installation Main Beams + CLT floor + (temporarily) Parapet January* 2024
- Final execution fase (3 months). Final approx. April 2024

Planning of Decommissioned Tracks (Treinvrijeperiode-TVP):


- Voornachten : 6 (gedeeltelijke onttrekking) (Q4-23/January 24)
- Main TVP : 76 hours. (incl buffer) – January 2024*

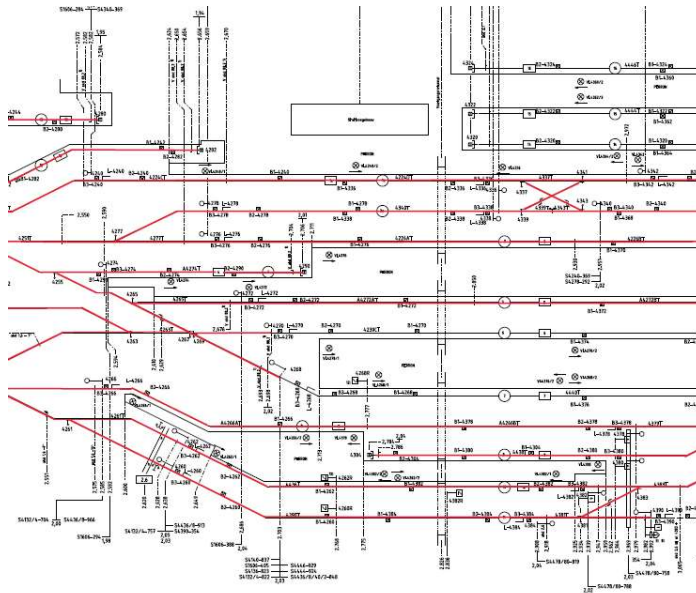

- Bus station approx. 6 days prior/during TVP
- Nanachten : 5 (gedeeltelijke onttrekking) – January – March 2024

Workspace :

- 2 locations :

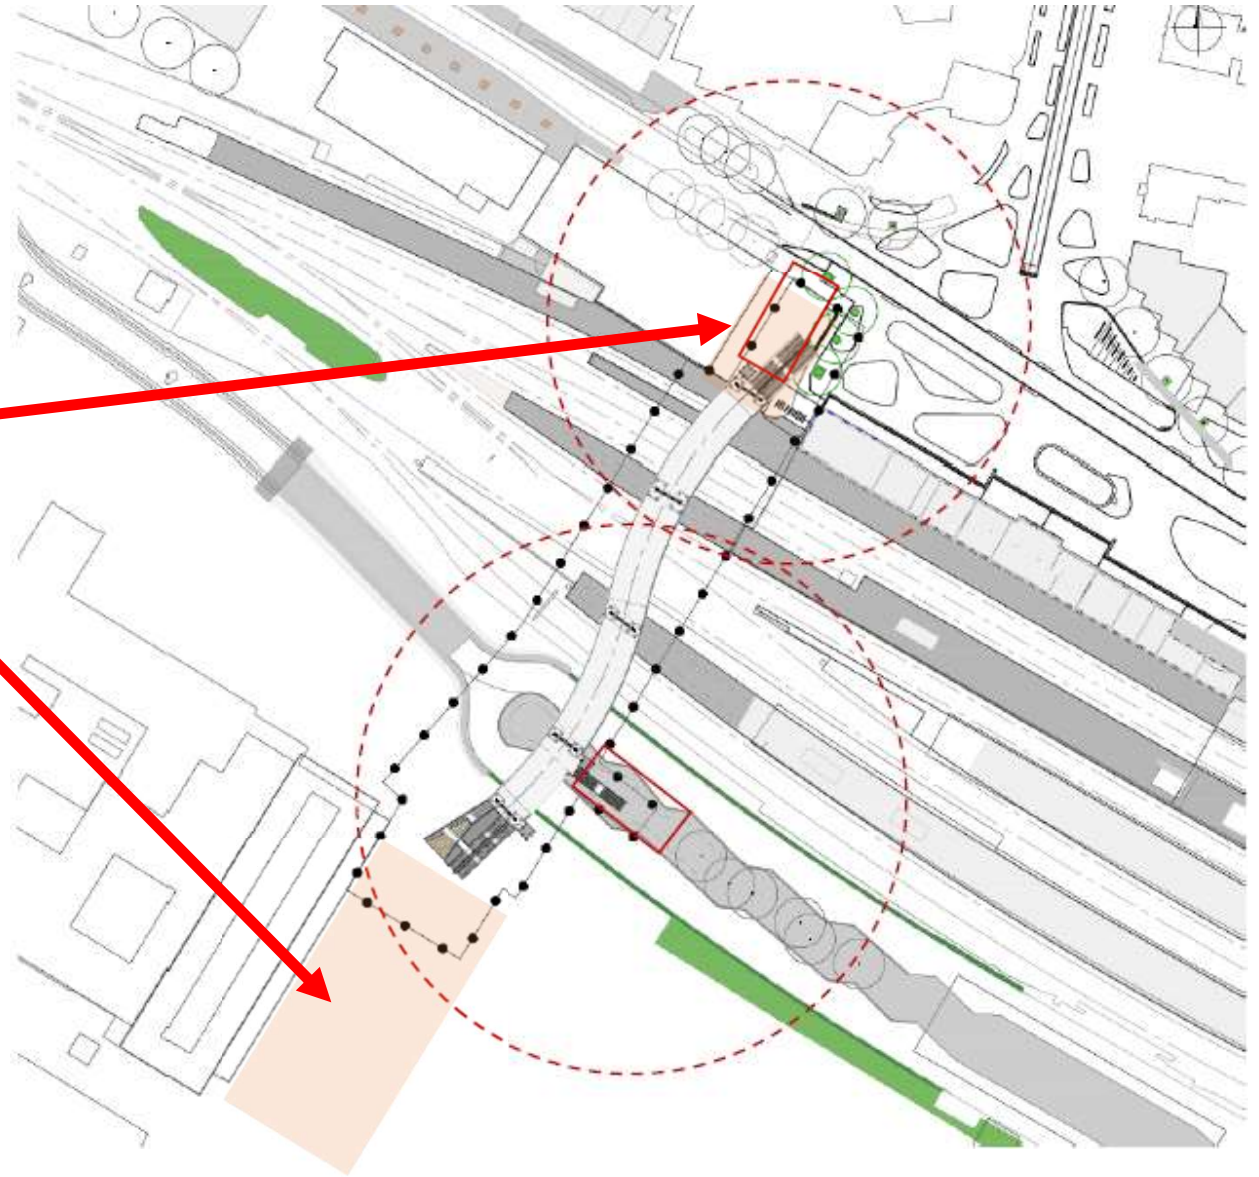

Routing / access :

