Id	Taaknaam	Duur	Begindatum	Einddatum	Voorafgaande taken
0	**108346 - TU/e Battery Storage**	**139 dagen**	**maa 29-4-24**	**don 28-11-24**	
1	**Work Preparation Fudura**	**67 dagen**	**maa 29-4-24**	**din 20-8-24**	
2	General preparation	4 wkn	maa 29-4-24	vri 24-5-24	
3	HSE (Health, Safety, Environment) plan	1 dag	maa 29-4-24	maa 29-4-24	
4	Staff instructions in case of emergencies	1 dag	maa 29-4-24	maa 29-4-24	
5	Lightning protection preparation	1 dag	maa 29-4-24	maa 29-4-24	
6	Cable calculation	5 dagen	maa 27-5-24	vri 31-5-24	2
7	Work Drawing	2 dagen	maa 3-6-24	din 4-6-24	6
8	Procurement of cables and other materials	8 wkn	woe 5-6-24	din 20-8-24	7
9	**Work Preparation TU/e**	**27 dagen**	**woe 21-8-24**	**don 26-9-24**	
10	Sending tender instructions	1 dag	woe 21-8-24	woe 21-8-24	8
11	Receiving offers	10 dagen	don 22-8-24	woe 4-9-24	10
12	Final awarding	1 dag	don 5-9-24	don 5-9-24	11
13	Delivery time	15 dagen	vri 6-9-24	don 26-9-24	12
14	**Execution Phase TU/e**	**6 dagen**	**vri 27-9-24**	**vri 4-10-24**	
15	Site planning preparation	5 dagen	vri 27-9-24	don 3-10-24	13
16	Installation of protective conduits	1 dag	vri 4-10-24	vri 4-10-24	15
17	Pruning trees and branches	1 dag	vri 4-10-24	vri 4-10-24	15
18	**Execution Phase Fudura**	**39 dagen**	**maa 23-9-24**	**don 14-11-24**	
19	**Medium Voltage Works**	**15 dagen**	**maa 23-9-24**	**vri 11-10-24**	
20	Excavation for CS compact station foundation	1 dag	maa 23-9-24	maa 23-9-24	17BE-10 dagen
21	Delivery and Placement of CS	1 dag	din 24-9-24	din 24-9-24	20
22	Excavation of MV cable trench	5 dagen	woe 25-9-24	din 1-10-24	21
23	Cable installation from CS to splice location	1 dag	woe 2-10-24	woe 2-10-24	22
24	Closing cable trench	3 dagen	don 3-10-24	maa 7-10-24	23
25	Cold assembly of MV	1 dag	din 8-10-24	din 8-10-24	24
26	Connection of CS into TU/e MV network	1 dag	woe 9-10-24	woe 9-10-24	25
27	Testing of MV cables	1 dag	don 10-10-24	don 10-10-24	26
28	Commissioning of Compact Station	1 dag	vri 11-10-24	vri 11-10-24	27
29	**Works PSU+AIO+BC+BC**	**24 dagen**	**maa 14-10-24**	**don 14-11-24**	
30	Delivery and placement of PCS+AIO+BC+BC	2 dagen	maa 14-10-24	din 15-10-24	28
31	Assembly and connection of AIO+BC+BC	2 dagen	woe 16-10-24	don 17-10-24	30
32	Cable installation from CS to PCS	2 dagen	vri 18-10-24	maa 21-10-24	31
33	Cable installation from PCS to AIO	2 dagen	din 22-10-24	woe 23-10-24	32
34	AC and DC cabling assembly	3 dagen	don 24-10-24	maa 28-10-24	33
35	Testing of AC and BC cabling	2 dagen	din 29-10-24	woe 30-10-24	34
36	SAT DELTA/Fudura	10 dagen	don 31-10-24	woe 13-11-24	35
37	Commissioning EOS	1 dag	don 14-11-24	don 14-11-24	36
38	**Project Completion**	**9 dagen**	**vri 15-11-24**	**woe 27-11-24**	
39	Resolving remaining issues	3 dagen	vri 15-11-24	din 19-11-24	37
40	Processing revision data	5 dagen	woe 20-11-24	din 26-11-24	39
41	Project evaluation	1 dag	woe 27-11-24	woe 27-11-24	40
42	Project closure	1 dag	don 28-11-24	don 28-11-24	41

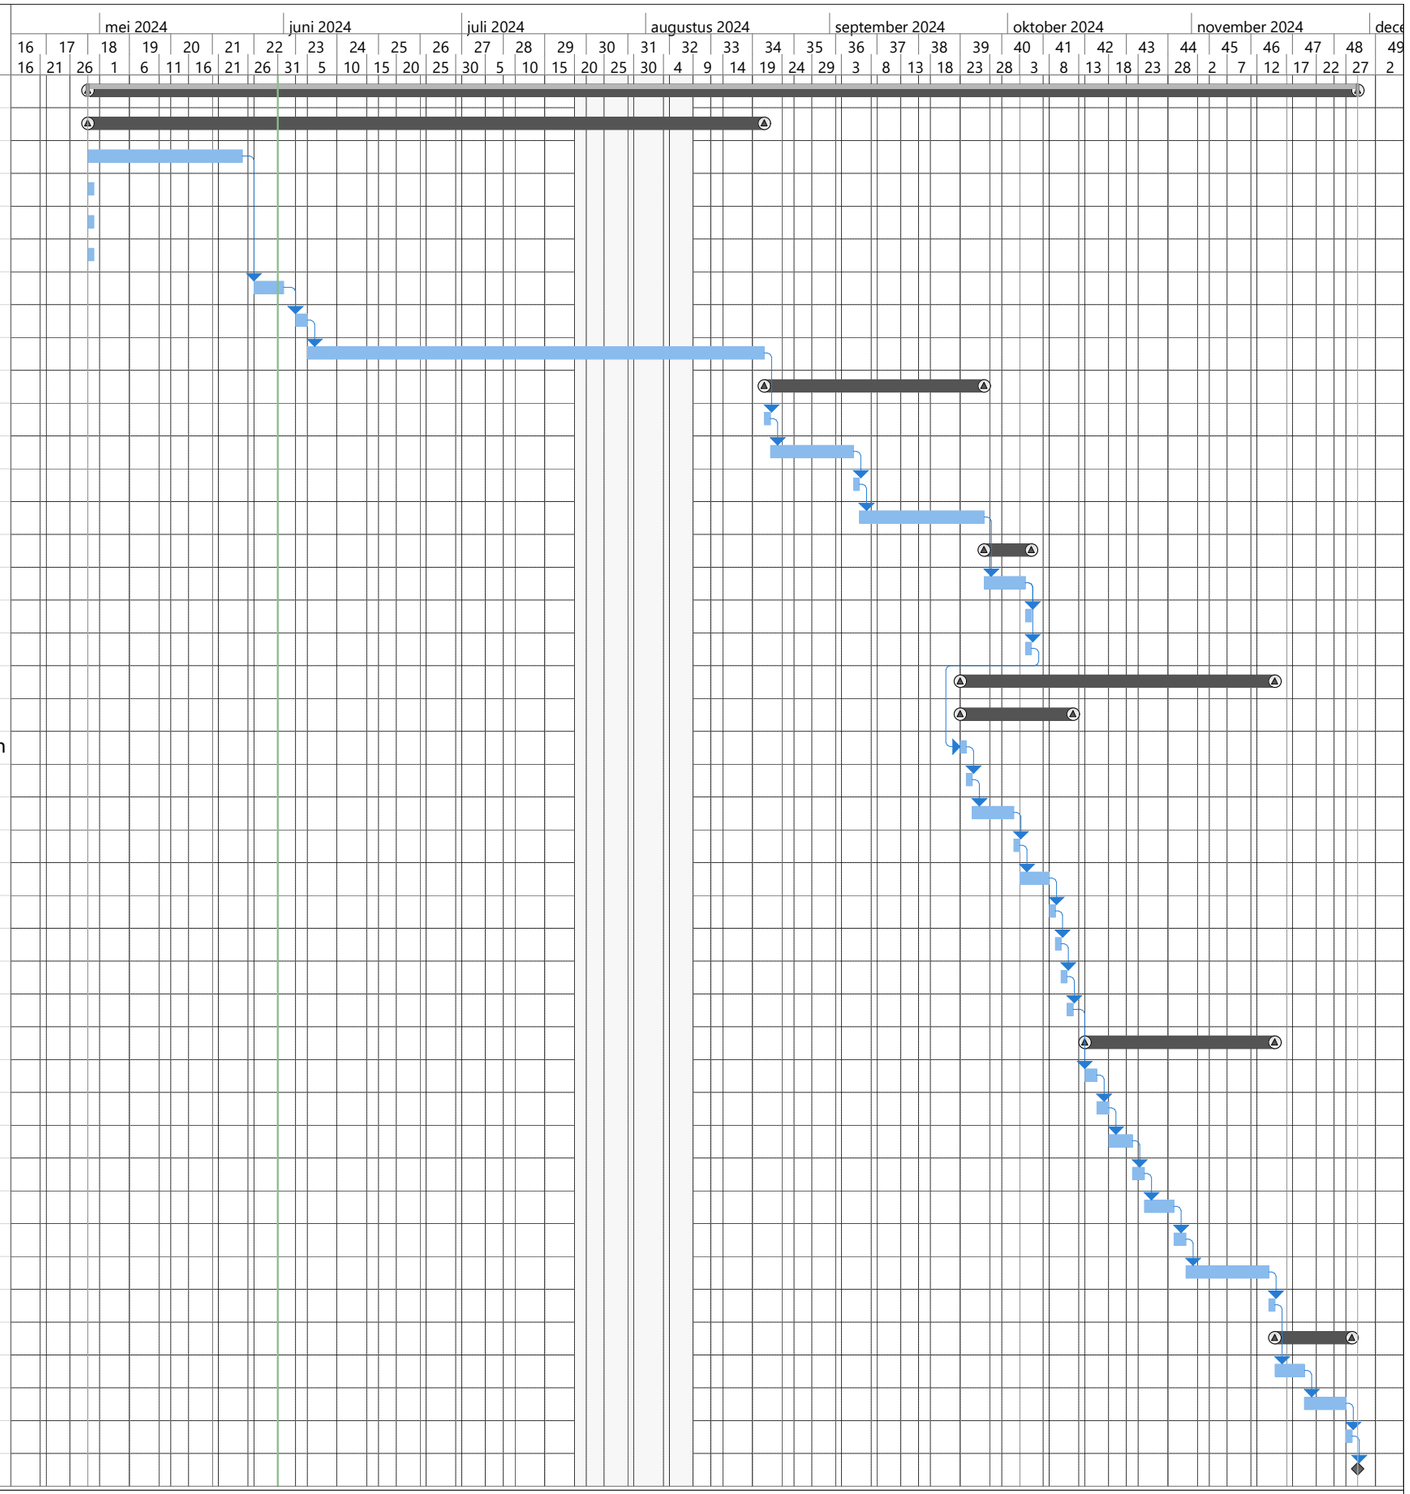

Project: 108346 - TU/e Battery S
Datum: vri 31-5-24

Taak | Splitsing | Mijlpaal | Samenvatting | Projectsamenvatting | Inactieve taken | Inactieve mijlpaal | Inactieve samenvatting | Handmatig taak | Alleen duur | Handmatige samenvatting | Handmatige samenvatting | Alleen begindatum | Alleen einddatum | Externe taken | Externe mijlpaal | Deadline | Voortgang | Voortgang, handmatig

Id	Taaknaam	Duur	Begindatum	Einddatum
0	**108346 - TU/e Battery Storage**	**139 dagen**	**maa 29-4-24**	**don 28-11-24**
1	**Work Preparation Fudura**	**67 dagen**	**maa 29-4-24**	**din 20-8-24**
2	General preparation	4 wkn	maa 29-4-24	vri 24-5-24
3	HSE (Health, Safety, Environment) plan	1 dag	maa 29-4-24	maa 29-4-24
4	Staff instructions in case of emergencies	1 dag	maa 29-4-24	maa 29-4-24
5	Lightning protection preparation	1 dag	maa 29-4-24	maa 29-4-24
6	Cable calculation	5 dagen	maa 27-5-24	vri 31-5-24
7	Work Drawing	2 dagen	maa 3-6-24	din 4-6-24
8	Procurement of cables and other materials	8 wkn	woe 5-6-24	din 20-8-24
9	**Work Preparation TU/e**	**27 dagen**	**woe 21-8-24**	**don 26-9-24**
10	Sending tender instructions	1 dag	woe 21-8-24	woe 21-8-24
11	Receiving offers	10 dagen	don 22-8-24	woe 4-9-24
12	Final awarding	1 dag	don 5-9-24	don 5-9-24
13	Delivery time	15 dagen	vri 6-9-24	don 26-9-24
14	**Execution Phase TU/e**	**6 dagen**	**vri 27-9-24**	**vri 4-10-24**
15	Site planning preparation	5 dagen	vri 27-9-24	don 3-10-24
16	Installation of protective conduits	1 dag	vri 4-10-24	vri 4-10-24
17	Pruning trees and branches	1 dag	vri 4-10-24	vri 4-10-24
18	**Execution Phase Fudura**	**39 dagen**	**maa 23-9-24**	**don 14-11-24**
19	**Medium Voltage Works**	**15 dagen**	**maa 23-9-24**	**vri 11-10-24**
20	Excavation for CS compact station foundation	1 dag	maa 23-9-24	maa 23-9-24
21	Delivery and Placement of CS	1 dag	din 24-9-24	din 24-9-24
22	Excavation of MV cable trench	5 dagen	woe 25-9-24	din 1-10-24
23	Cable installation from CS to splice location	1 dag	woe 2-10-24	woe 2-10-24
24	Closing cable trench	3 dagen	don 3-10-24	maa 7-10-24
25	Cold assembly of MV	1 dag	din 8-10-24	din 8-10-24
26	Connection of CS into TU/e MV network	1 dag	woe 9-10-24	woe 9-10-24
27	Testing of MV cables	1 dag	don 10-10-24	don 10-10-24
28	Commissioning of Compact Station	1 dag	vri 11-10-24	vri 11-10-24
29	**Works PSU+AIO+BC+BC**	**24 dagen**	**maa 14-10-24**	**don 14-11-24**
30	Delivery and placement of PCS+AIO+BC+BC	2 dagen	maa 14-10-24	din 15-10-24
31	Assembly and connection of AIO+BC+BC	2 dagen	woe 16-10-24	don 17-10-24
32	Cable installation from CS to PCS	2 dagen	vri 18-10-24	maa 21-10-24
33	Cable installation from PCS to AIO	2 dagen	din 22-10-24	woe 23-10-24
34	AC and DC cabling assembly	3 dagen	don 24-10-24	maa 28-10-24
35	Testing of AC and BC cabling	2 dagen	din 29-10-24	woe 30-10-24
36	SAT DELTA/Fudura	10 dagen	don 31-10-24	woe 13-11-24
37	Commissioning EOS	1 dag	don 14-11-24	don 14-11-24
38	**Project Completion**	**9 dagen**	**vri 15-11-24**	**woe 27-11-24**
39	Resolving remaining issues	3 dagen	vri 15-11-24	din 19-11-24
40	Processing revision data	5 dagen	woe 20-11-24	din 26-11-24
41	Project evaluation	1 dag	woe 27-11-24	woe 27-11-24
42	Project closure	1 dag	don 28-11-24	don 28-11-24

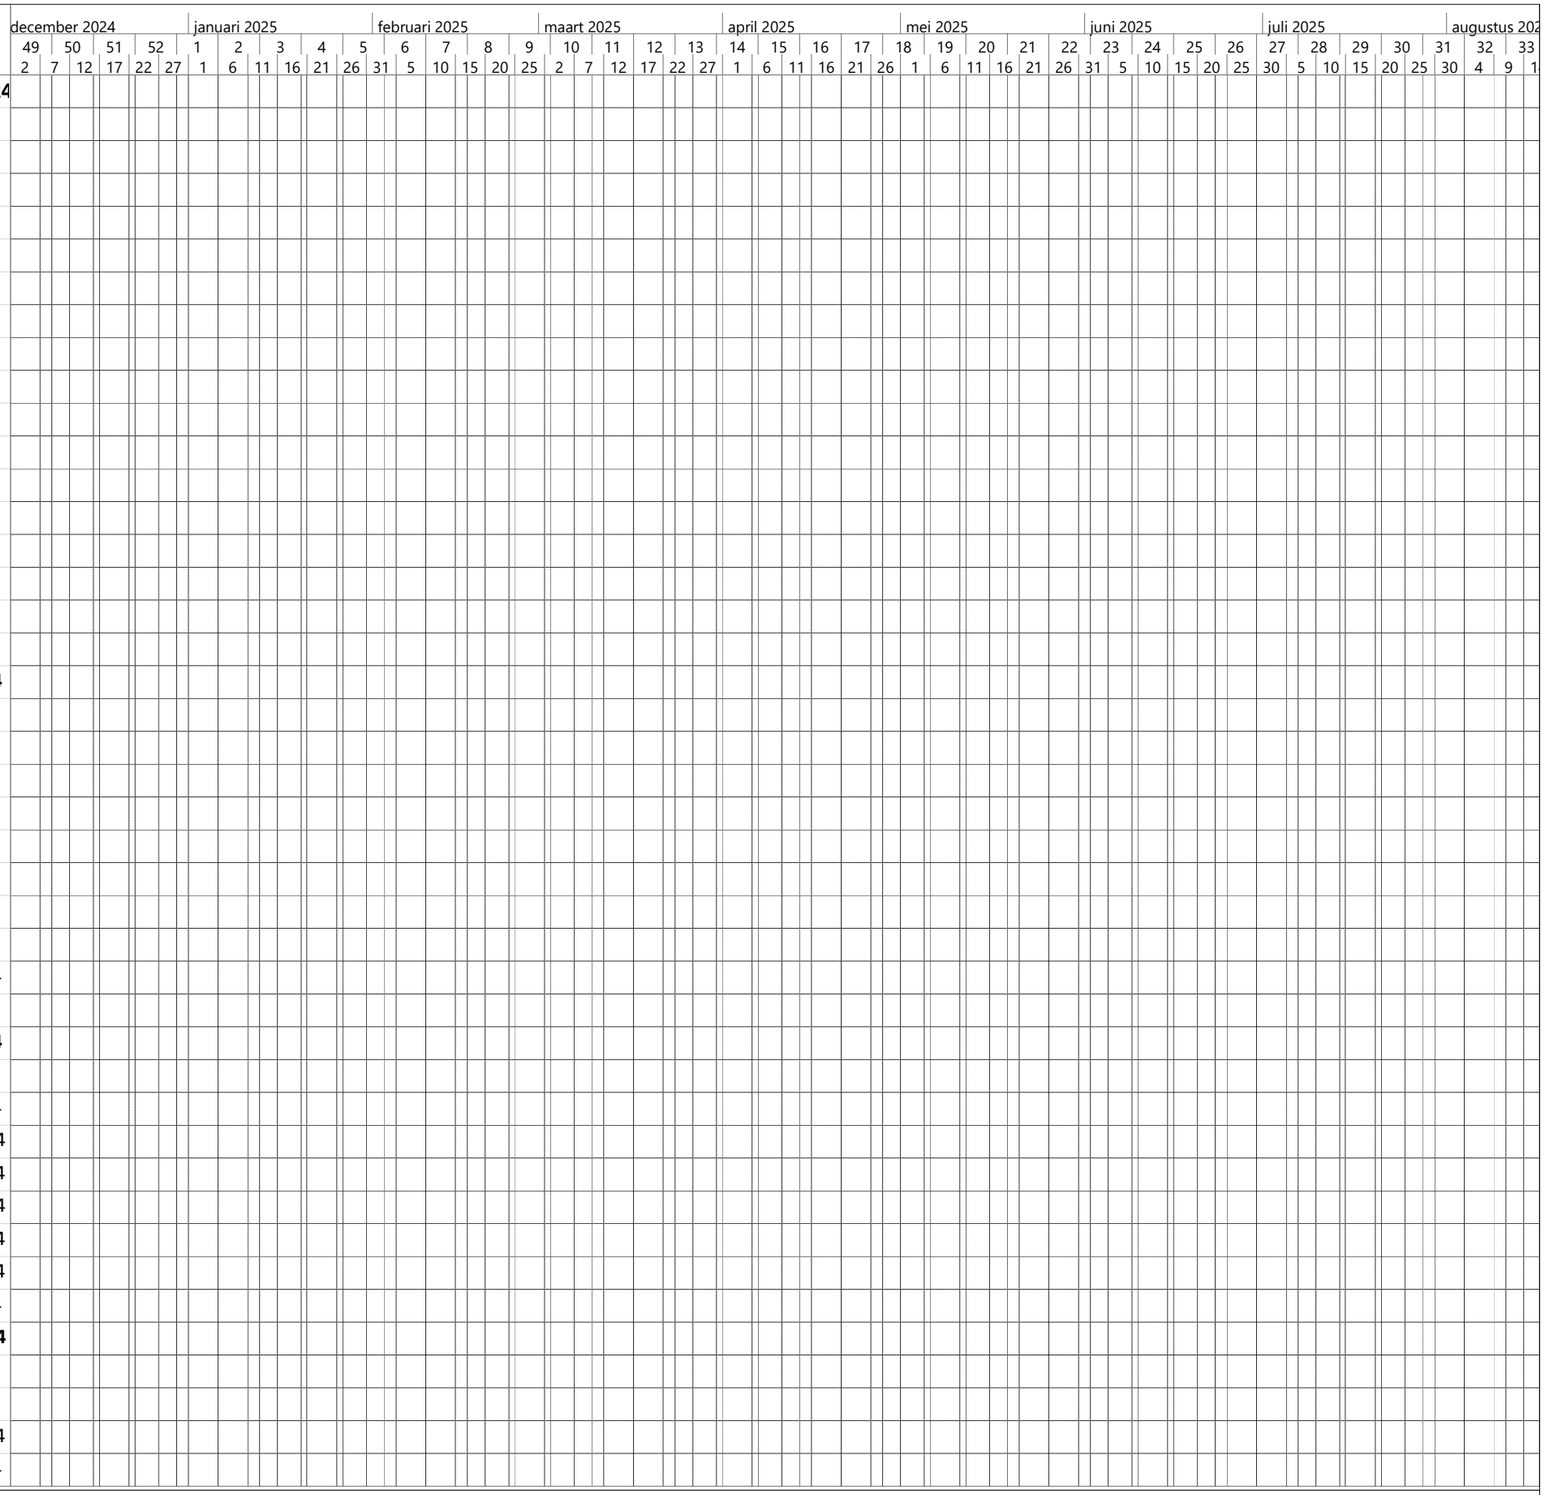

Project: 108346 - TU/e Battery S
Datum: vri 31-5-24

Taak	Projectsamenvatting	Handmatig taak	Alleen begindatum	Deadline
Splitsing	Inactieve taken	Alleen duur	Alleen einddatum	Voortgang
Mijlpaal	Inactieve mijlpaal	Handmatige samenvatting	Externe taken	Voortgang, handmatig
Samenvatting	Inactieve samenvatting	Handmatige samenvatting	Externe mijlpaal	
